

**Forest North Drainage Improvement Project
October 2016**




Dear Neighbor,

You are receiving this email because you signed up for regular updates on the Forest North Drainage Improvement Project or are located within a zone where construction work is taking place or is soon to begin.

DeNucci Constructors, LLC continues work in the Tichester and Sherbrooke zones. Water line relocation continues at the Meadowheath Drive /Sherbrooke Street intersection with a scheduled completion in two weeks. Pipe installation and rock excavation for storm sewers in the Sherbrooke zone continues along Sherbrooke Street and Meadowheath Drive. Asphalt repairs have begun on Meadowheath Drive and Briar Hollow Drive and completion is anticipated in two weeks. Seeding and installing an erosion control blanket along Meadowheath Drive, Haversham Court and Briar Hollow Drive is expected to begin in two weeks.

The Tichester (yellow) and Sherbrooke (green) zones are highlighted in the image below. A larger map of the neighborhood and the work zones can be found [here](#).

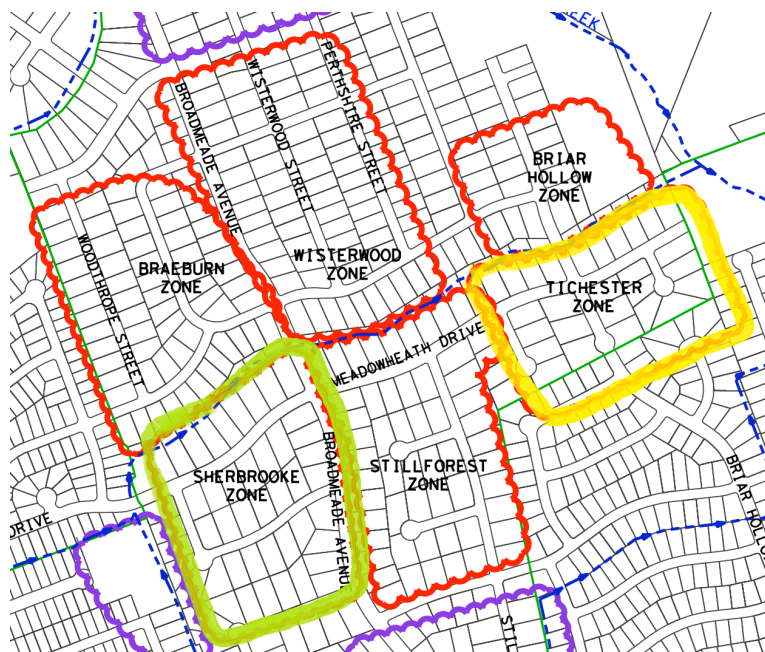

Members of the construction team have made or will make door-to-door visits prior to actual construction in each zone. Vehicles parked on the street may need to be relocated while work occurs. Please, continue to visit the [project website](#) for updates.

Utility Relocations

AT&T relocations are ongoing in the Braeburn, Wisterwood and Briar Hollow zones. Crews have completed placement of new lines in the existing easements, and will be splicing them into the existing system.

Tichester and Sherbrooke Zone Residents:

Residents in the construction area have received notifications about the project and a door hanger regarding homeowner items in the right-of-way. If you wish to preserve these items (custom mailboxes, landscaping, planters, trees, irrigation systems, etc.), it is suggested you begin removing them now from the right-of-way. If homeowner items are not removed by the time construction begins, then the contractor will consider these items left for refuse.

Mailboxes: Mailboxes in the path of drainage work will be removed and replaced with standard units. We are in close communication with the post office to ensure there is no disruption of mail service.

Driveways: The re-grading of channels and replacement of driveway culverts will require the re-construction of some driveways. Driveways will be accessible by the end of each workday. Full driveway repairs will be made upon completion of the entirety of the work at each property. Notice will be provided to homeowners and residents at least 48 hours prior to any driveway-access interruptions.

Irrigation Systems: Irrigation systems in the path of drainage work will be removed, capped at the right-of-way line and will not be replaced.

Questions, Subscribe to Email Alerts and Project Webpage

If you have any questions regarding this information, please contact our Public Involvement Team by calling (512) 943-1195 or emailing roads@wilco.org. All project materials and updates, including any lane or road closures, will be posted on the Forest North Drainage Improvement Project page of the Road Bond website. We encourage you to sign up for news and updates under the “Subscriptions” tab.

Forest North Drainage Improvement Project web link: www.roadbond.org/forestnorth

Sincerely,

The Williamson County Public Involvement Team
Phone: (512) 943-1195
Email: roads@wilco.org
